



CONSTRUCTION UPDATE

December 7, 2021

UPCOMING CONSTRUCTION ACTIVITIES

El Camino Real (ECR) Lane Closures

ECR work continues intermittently according to this approximate construction schedule:

- **Sanitary Sewer Line Installation:** Completed
- **Hydrant Installations:** Completed
- **Storm Line Installation:** Completed
- **Water Line Installation:** Completed
- **Pipe Work and Testing:** Completed
- **Roadway Repaving:** January–February 2022

Other Offsite Impacts

- Sidewalk and street improvement work continues.

Office Buildings

Building 1

- Stucco installation is scheduled to be completed by 12/17.
- Roof tile and membrane installations continue.
- Interior work on the core revisions and additional elevators continues.

Building 2

- Stairway handrails and cable rails installation is ongoing.
- Exterior and interior painting continues.
- Waterproofing of the ground-level concrete deck continues. Concrete pours for planter boxes, sidewalks, curbs and gutter near the train tracks are ongoing.
- Installation of the balcony pedestal pavers continues.
- Parking lot and access road grading continues.

Building 3

- Concrete pours for sidewalks, curbs and gutters near the train tracks are ongoing.
- Parking lot and access road grading continues.

CONTACT INFORMATION

Construction Information Line
(650) 497-4052


Email
middleplaza@stanford.edu

Website
middleplaza.stanford.edu

On-site Construction Manager
Nic Durham
ndurham@stanford.edu
(650) 725-2960

City of Menlo Park
(650) 330-6704

After Hours/Emergency
911

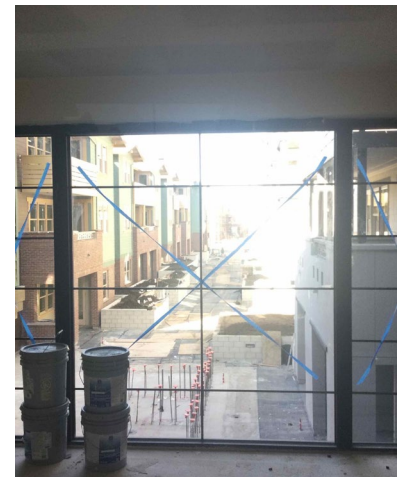

Glass installed for Building B storefront frames

Thanks for your patience during construction



UPCOMING CONSTRUCTION ACTIVITIES (continued)

Residential Buildings & Pool

- Exterior sheathing, roofing, detailing, and inspections continue.
- Solar panel installation continues.
- Exterior painting for Building C has completed; electrical installations will follow.
- Wood framing is nearing completion for Building A.
- Interior construction and inspections for Building A, B and C continue.
- Siding, weatherproofing, and painting on Building B exterior continues.
- Bridge construction and waterproofing continues at Buildings A, B and C.
- Balcony railing work continues.
- Forming of the pool continues.

Garage

- Electrical room construction for Building A has completed.
- Insulation, shoring, steel, and temporary supporting structure erection is ongoing.
- HVAC and electrical inspections continue.
- Seismic bracing continues.

Stormwater Drainage System

- Water tie-in is set to begin following the completion of water line installations for Office Buildings 2 and 3.
- Bioswale and onsite landscaping will follow.



Middle Plaza Site Plan

CONTACT INFORMATION

Construction Information Line
(650) 497-4052

Email
middleplaza@stanford.edu

Website
middleplaza.stanford.edu
